

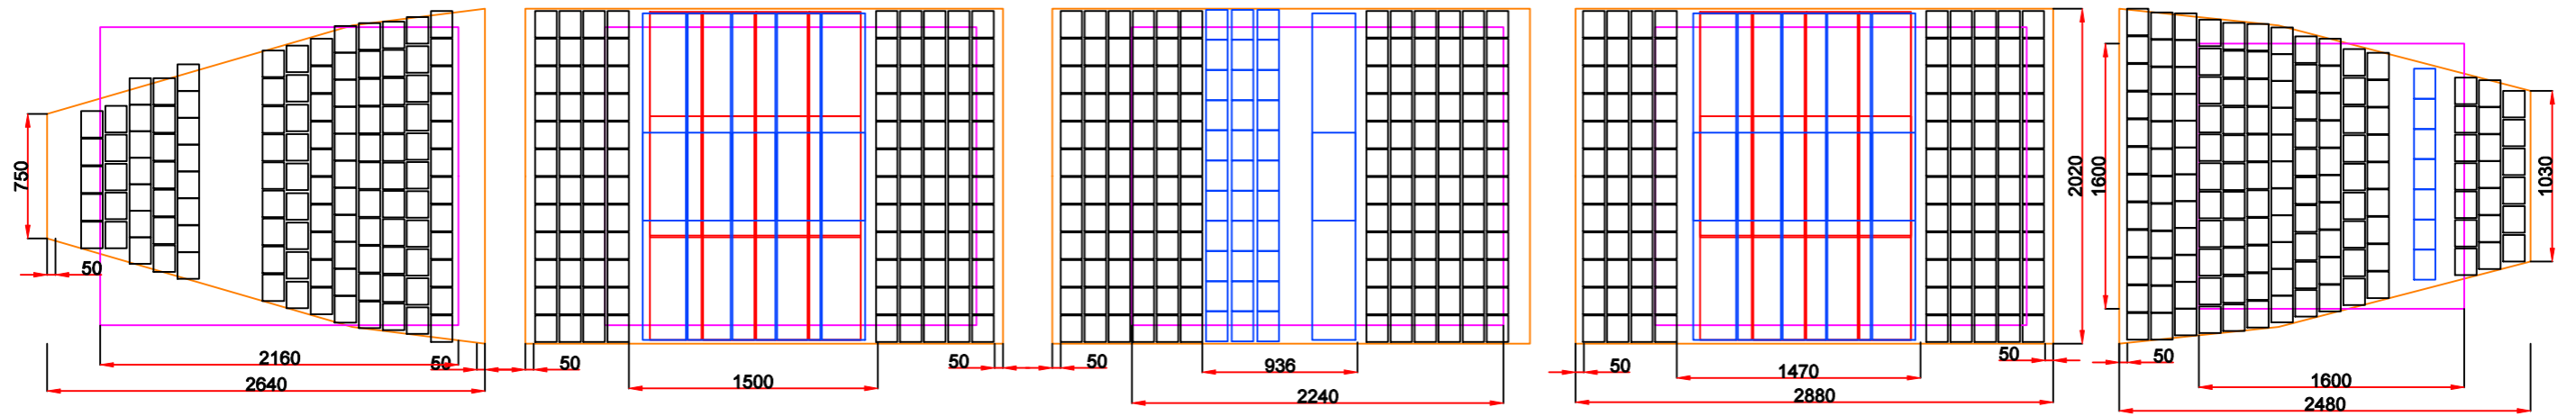


TOP VIEW

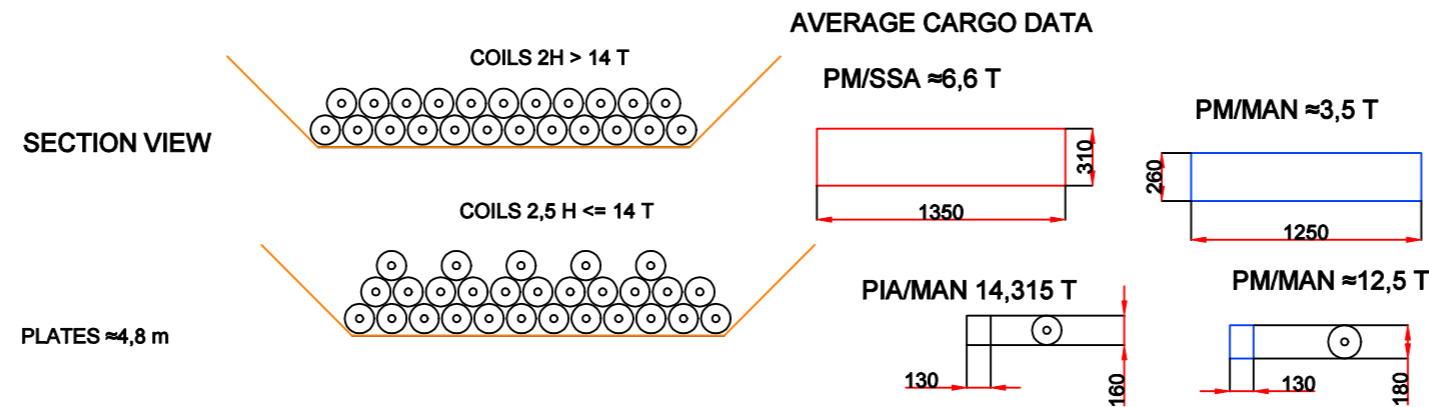

t/ho	coils/ho	PM/SSA		PM/MAN		PIA/MAN		FWD / CENTER				AFT / CENTER					
		TONS	PLATES	TONS	COILS	TONS	COILS	TONS	PLATES	TON	COILS	TONS	COILS				
HO 1	4874	350		216	13	950	69	PIA - T 4 L - 2,5-3 H + PM (1Lx13@>12,5 T) T 1 L - 2H				3708	268	PIA-T 10 L / 2,5-3 h			
HO 2	7002	315	1250	188		2170	169	PIA - T 5 L / 2-2,5 H + PM 2 STACKS ≈94 T / ≈ 0,4 M+2 STACKS x ≈625 T ≈4,2 M				1250	282	PIA - T 4 L / 2-2,5 H + PM 3 STACKS ≈94 T / ≈ 0,4 M+2 STACKS x ≈625 T ≈4,2 M			
HO 3	6000	373		200		2449	148	PIA - T 6 L / 2-2,5 H + PM 1 STACK ≈ 200 T / ≈ 200				880	75	PIA - T 6 L / 2-2,5 H + PM (2Lx28@>12,5 T) 3H+(1Lx19@>12,5 T) 2H - T 3 L / 3-2 H			
HO 4	6257	261	1250	188		1884	149	PIA - T 5 L / 2-2,5 H + PM 2 STACKS ≈94 T / ≈ 0,4 M+2 STACKS x ≈625 T ≈4,2 M				1250	282	PIA - T 4 L / 2-2,5 H + PM 3 STACKS ≈94 T / ≈ 0,4 M+2 STACKS x ≈625 T ≈4,2 M			
HO 5	4140	221				4140	221	PIA-T 13 L / 2-2,5 H				0		INCLUDED			
TOTAL	28273	1520	2500	0	792	13	11593	756					2500	1444	75	9444	676

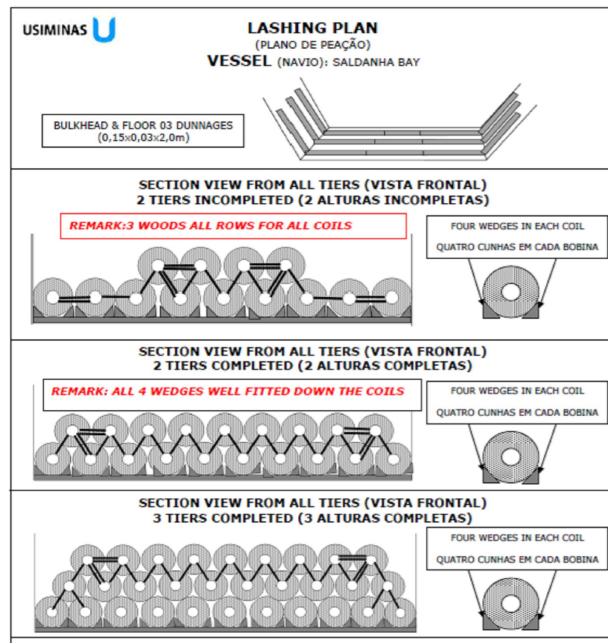

TOTAL - EXPECTED
 21037 T ST COILS PIA-MAN
 2230 T ST COILS/PLATES (1096/1134) PM-MAN
 5000 T ST PLATES PM-SSA

 Emissão FELIPE GUERRA	Registro ITM 27-05/21-002	Revisões R1 28/05/21 R2 29/05/21 R3 02/06/21 R4 10/06/21
	Aprovado	Escala cm
MV CLIPPER COPENHAGEN 22000 T ST COILS + 5000 T ST PLATES PIA-PM-SSA-MAN		
SUBJECT TO FINAL PACKING LIST		

Remarks:
 1- Stowage of coils was calculated basis 2-3 H, but when possible with light coils (<=14 t) to be performed 2,5 H for save space never exceeding the tank-top strength (20 t / m²) and stack load of 36 T.
 2- No height limitation for the plates if not exceeding the strength of the tktop and shippers standard stowage and lasing.
